

Weekly Update: Week of October 7, 2024

Reference: District of Ucluelet – Peninsula Road Improvements (Phase 1)

Activities for the weeks of September 23 to October 4:

- Peninsula Roadway Improvements – Section #3 Paving
 - Asphalt Removal – Completed Week of September 23
 - Clearing / Trimming for Roadway Widening – Completed Week of September 23
 - Proof Roll – Completed Week of September 23
 - Asphalt Paving (Base Lift) – Completed Week of September 23
 - Asphalt Paving (Top Lift) – Completed Week of September 30

Upcoming Activities:

- Install Groundwater Drain at Sta 0+830 m – Week of October 7
- Install RRFB Bases & Signs (Pedestrian Crossings) – Week of October 7
- Painting Markings Peninsula Road Paving (Section 3) – Week of October 7

See Attached Progress Photos 1 – 14



Photo #1 – Asphalt Removal (Milling)



Photo #2 – Asphalt Removal (Milling)



Photo #3 – Asphalt Removal (Milling)



Photo #4 – Clearing / Trimming for Roadway Widening



Photo #5 – Asphalt Paving (Base Lift)



Photo #6 – Asphalt Paving (Base Lift)



Photo #7 – Asphalt Paving (Base Lift)

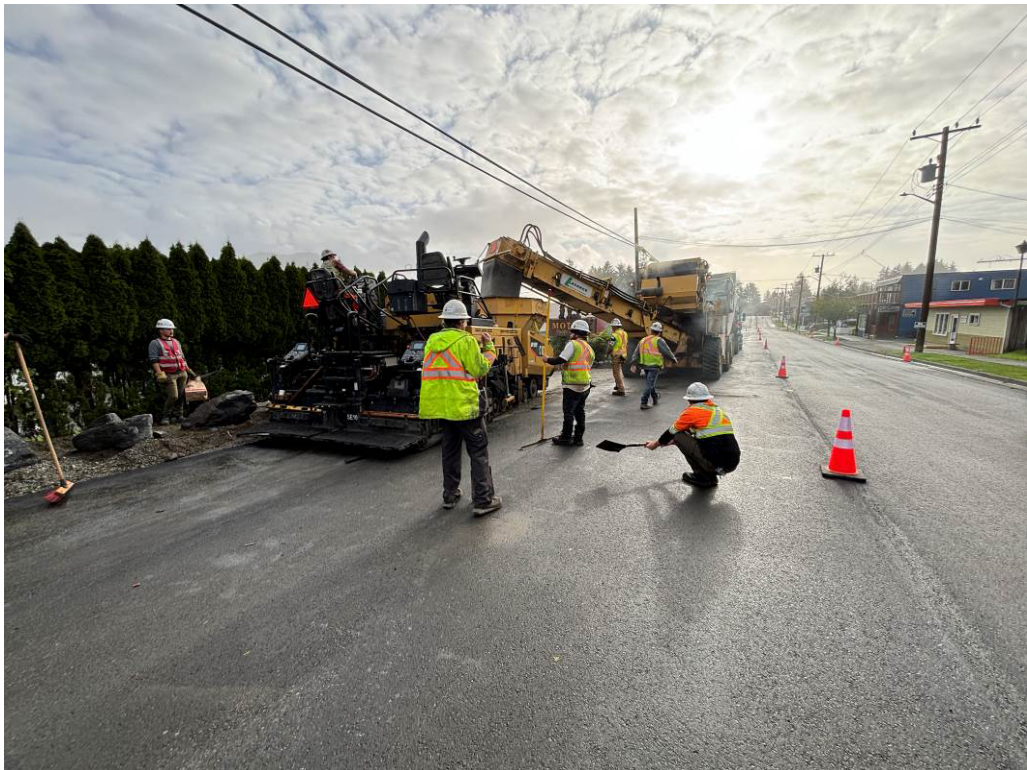


Photo #8 – Asphalt Paving (Base Lift)



Photo #9 – Asphalt Paving (Base Lift)



Photo #10 – Asphalt Paving (Top Lift)



Photo #11 – Asphalt Paving (Top Lift)



Photo #13 – Asphalt Paving (Top Lift)



Photo #13 – Asphalt Paving (Top Lift)

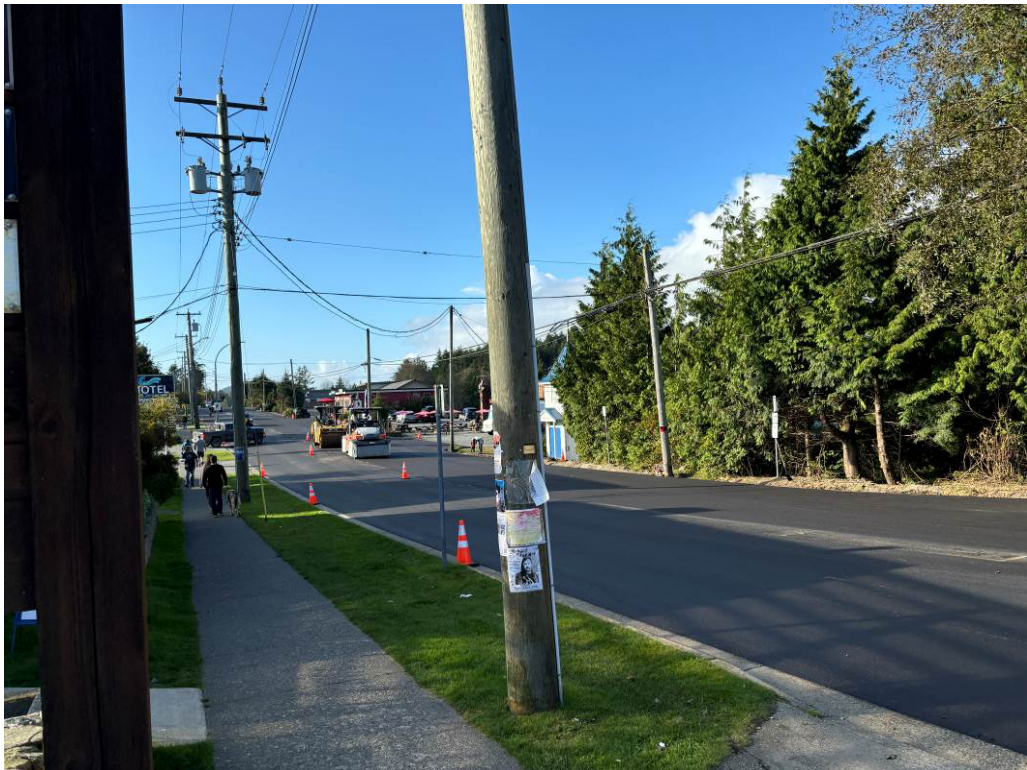


Photo #14 – Asphalt Paving (Top Lift)
