DoU Lift Stations - Preliminary Construction Schedule

ID	Task Name	Duration	Start	Finish
1	**Ucluelet Sewage Upgrades**	**154 days**	**Mon 1/5/26**	**Thu 8/6/26**
2	Contract Execution	1 day	Mon 1/5/26	Mon 1/5/26
3	Submittals & Drawing Reviews	30 days	Tue 1/6/26	Mon 2/16/26
4	Kickoff Meeting	1 day	Tue 1/20/26	Tue 1/20/26
5	Contract 1 - Pump Station - Lead Time	60 days	Tue 2/17/26	Mon 5/11/26
6	Contract 1 - Pumps - Lead Time	70 days	Tue 2/17/26	Mon 5/25/26
7	Contract 1 - Generator - Lead Time	120 days	Tue 2/17/26	Mon 8/3/26
8	Contract 1 - Kiosk - Lead Time	90 days	Tue 2/17/26	Mon 6/22/26
9	Contract 2A - Pumps lead time	70 days	Tue 2/17/26	Mon 5/25/26
10	Contract 2A - Electrical (VFDs / Control Cabinet) -	70 days	Tue 2/17/26	Mon 5/25/26
11	Contract 2A - Flow meter chamber - Lead Time	70 days	Tue 2/17/26	Mon 5/25/26
12	Utility Locates	1 day	Thu 1/22/26	Thu 1/22/26
13	Contract 2A - Forcemain	10 days	Fri 1/23/26	Thu 2/5/26
14	Contract 2B - Sanitary Sewer	4 days	Fri 2/6/26	Wed 2/11/26
15	Contract 2B - Tie-In	1 day	Thu 2/12/26	Thu 2/12/26
16	Contract 2 A/B - Surface Restorations	4 days	Fri 2/13/26	Wed 2/18/26
17	Contract 3 A/B - Sanitary Sewer	8 days	Thu 2/19/26	Mon 3/2/26
18	Contract 3 A/B - Storm	1 day	Tue 3/3/26	Tue 3/3/26
19	Contract 3 A/B - Surface Restorations	5 days	Wed 3/4/26	Tue 3/10/26
20	Contract 1 - Gravity Sewer	10 days	Wed 4/1/26	Tue 4/14/26
21	Contract 1 - Forcemain	4 days	Wed 4/15/26	Mon 4/20/26
22	Contract 1 - Water & Storm	3 days	Tue 4/21/26	Thu 4/23/26
23	Contract 1 - Surface Restoration	3 days	Fri 4/24/26	Tue 4/28/26
24	Contract 1 - Pump Station Civil / Mechanical	15 days	Tue 5/5/26	Mon 5/25/26
25	Contract 1 - Pump Station Electrical	5 days	Tue 6/23/26	Mon 6/29/26
26	Contract 1 - Commissioning	3 days	Tue 6/30/26	Thu 7/2/26
27	Contract 1 - Tie-Ins	2 days	Fri 7/3/26	Mon 7/6/26
28	Contract 2A - Pump Station Civil / Mechanical	7 days	Tue 5/26/26	Wed 6/3/26
29	Contract 2A - Pump Station Electrical	5 days	Thu 6/4/26	Wed 6/10/26
30	Contract 2A - Commissioning	3 days	Thu 6/11/26	Mon 6/15/26
31	Contract 2A - Tie-Ins	3 days	Tue 6/16/26	Thu 6/18/26
32	Final Paving / Surface Resto	2 days	Fri 6/19/26	Mon 6/22/26
33	Cleanup & Demob	3 days	Tue 6/23/26	Thu 6/25/26
34	Generator Install	3 days	Tue 8/4/26	Thu 8/6/26

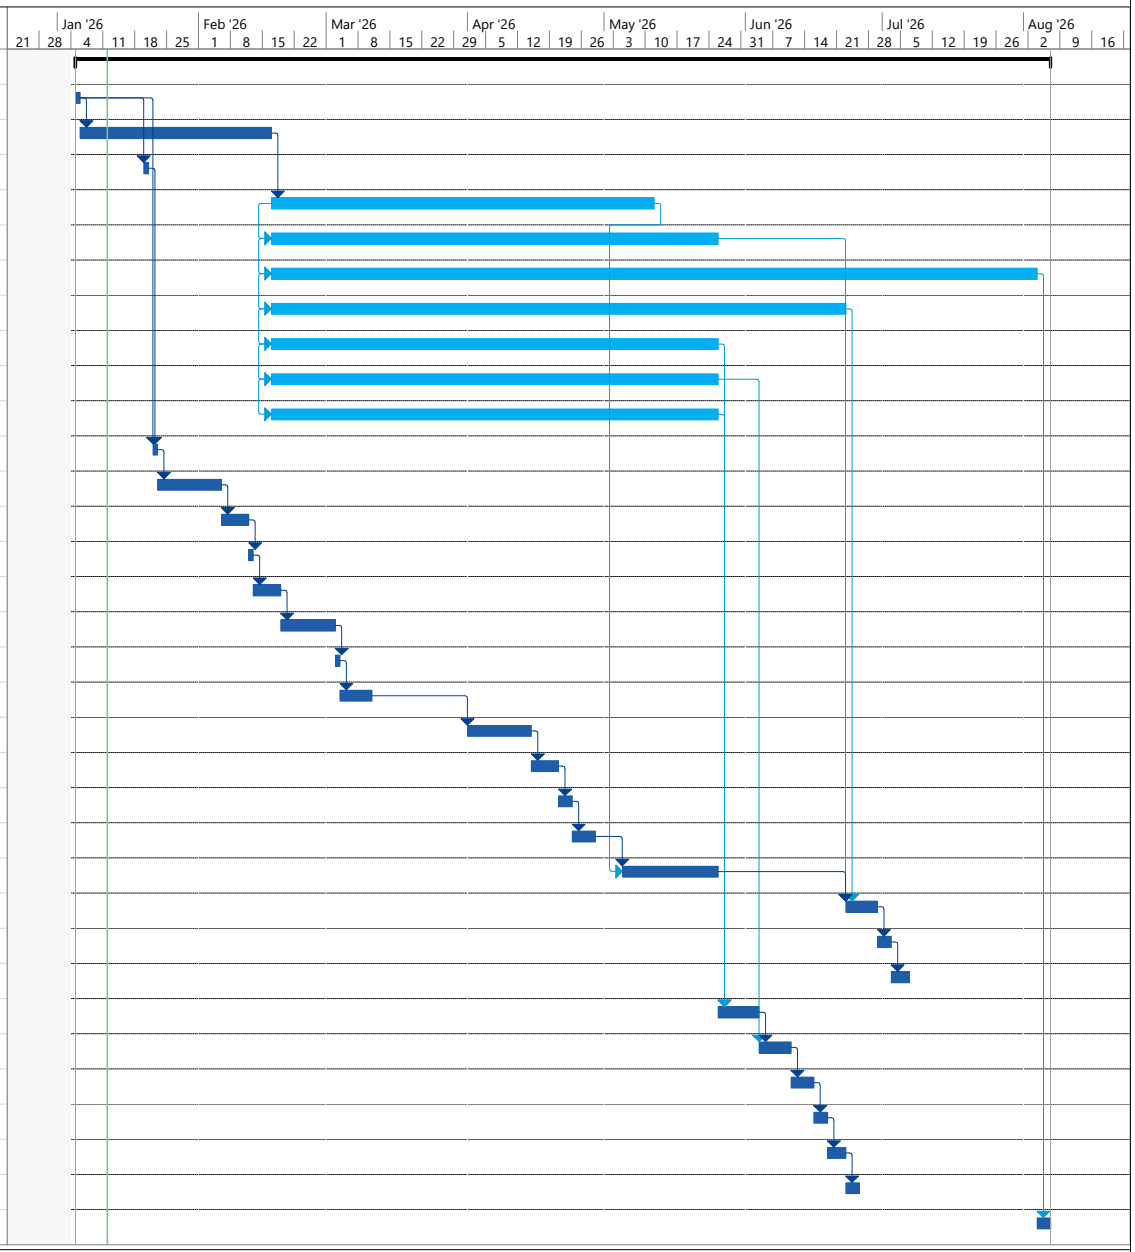

Project: Preliminary Constructio
Date: Mon 1/12/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
